

## Weeks 50–51

### Work area Building 10

- Filling for building foundation of Building 10.
- Foundation work for link building between Building 1 and Building 10.

### Work area Building 9

- Building of walls on floor 0.
- Joist work over floor 0, in stages like previous work.
- Covering windows and glass sections Building 1, floor 1.
- Hole work in K1 by Building 1 for pipes.
- Insulation of facade floor 1.
- Refilling soil toward the building.

### Work area Building 1(Existing Ångström)

- Covering windows and glass sections Building 1, facing construction Building 9.
- Connections, installations with associated work in rooms 1K2647, 1K2655 and 1K2962.

### Traffic

- Heavy traffic in connection with construction by Building 9 and excavation by Building 10.

### Disturbances

- Heavy traffic.
- Noise from equipment associated with construction.
- Drilling in facade for attachment of moulds and insulation. This work will primarily occur outside of normal business hours, but drilling can also occur during daytime. The extent of this work, however, is not more than previous work.
- Refilling of soil toward Building 9 can result in noise and vibrations in Building 1 and Freia.

### Closures, provisional arrangements

- According to general plan.
- Work in rooms 1K2647, 1K2655 and 1K2962.
- Minor closures in Building 1 when windows and window sections are being covered facing the construction.


### Noticeable upcoming work (preliminary start times)

- Work to remove plaster, insulation of existing walls and attaching moulds for walls facing Building 1 will be done by floor until the middle of March 2019. Window sections and windows facing the construction will be covered again by floor in connection with the above work.


*Construction management for NCC and Akademiska Hus*

---

**Parkeringen avstängd från och med måndag 19/11.**

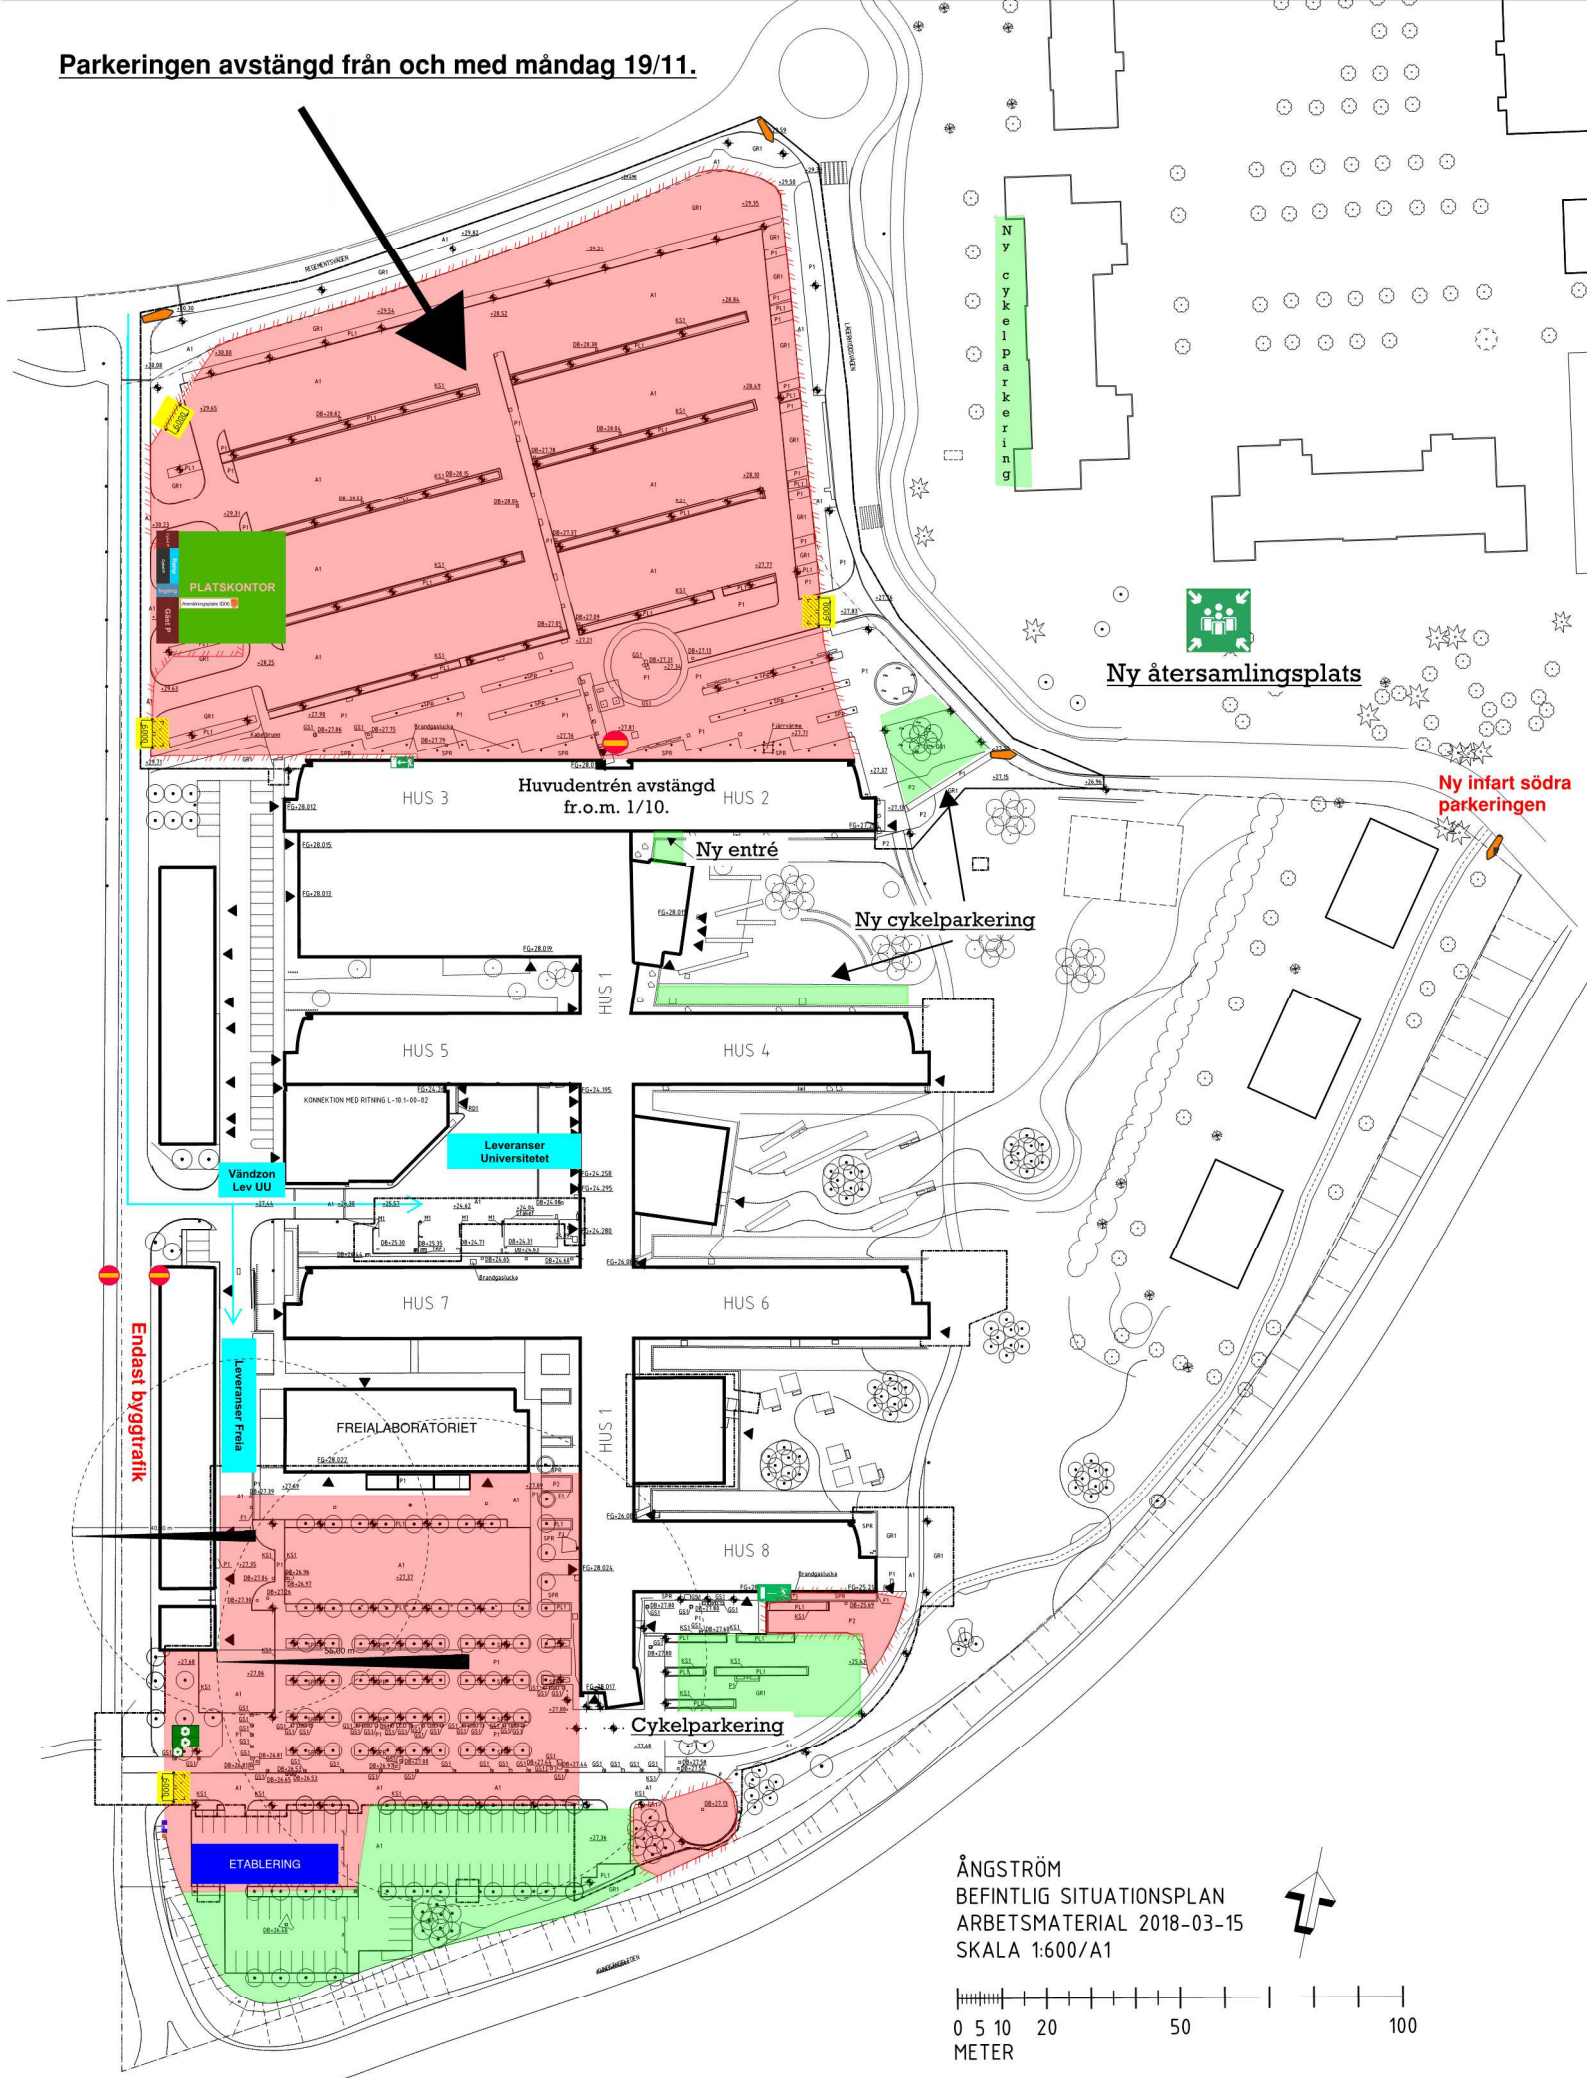

ÅNGSTRÖM  
BEFINTLIG SITUATIONSPLAN  
ARBETSMATERIAL 2018-03-15  
SKALA 1:600/A1



APD-plan Å4  
NCC  
2018-12-04
