

Weeks 52–03

Work area Building 10

- Large excavation for foundation of Building 10 begins week 2.
- Foundation work for link building between Building 1 and Building 10.

Work area Building 9

- Building of walls on floor 1.
- Joist work over floor 0, in stages like previous work.
- Covering windows and glass sections Building 1, floor 2.
- Refilling soil toward the building.
- Removal of facade Building 1 towards Building 9 floor 2 during weeks 4–5.

Work area Building 1(Existing Ångström)

- Connections, installations with associated work in rooms 1K2647, 1K2655 and 1K2962.
- Removal of facade on floor 2 towards Building 9 during weeks 4–5.

Traffic

- Heavy traffic in connection with construction by Building 9 and excavation by Building 10.

Disturbances

- Heavy traffic.
- Noise from equipment associated with construction.
- Drilling in facade for attachment of moulds and insulation. This work will occur primarily outside of normal business hours, but drilling can also occur during daytime. The extent of this work, however, is not more than previous work.
- Refilling of soil toward Building 9 can result in noise and vibrations in Building 1 and Freia.

Closures, provisional arrangements


- According to general plan.
- Rooms 1K2647, 1K2655 and 1K2962.
- Minor closures in Building 1 when windows and window sections facing the construction are being covered.

Noticeable upcoming work (preliminary start times)


- Work to remove plaster, insulation of existing walls and attaching moulds for walls facing Building 1 will be done floor-by-floor until the middle of March 2019. Window sections and windows facing the construction will be covered floor-by-floor in connection with the above work.

Construction management for NCC and Akademiska Hus

Parkeringen avstängd från och med måndag 19/11.

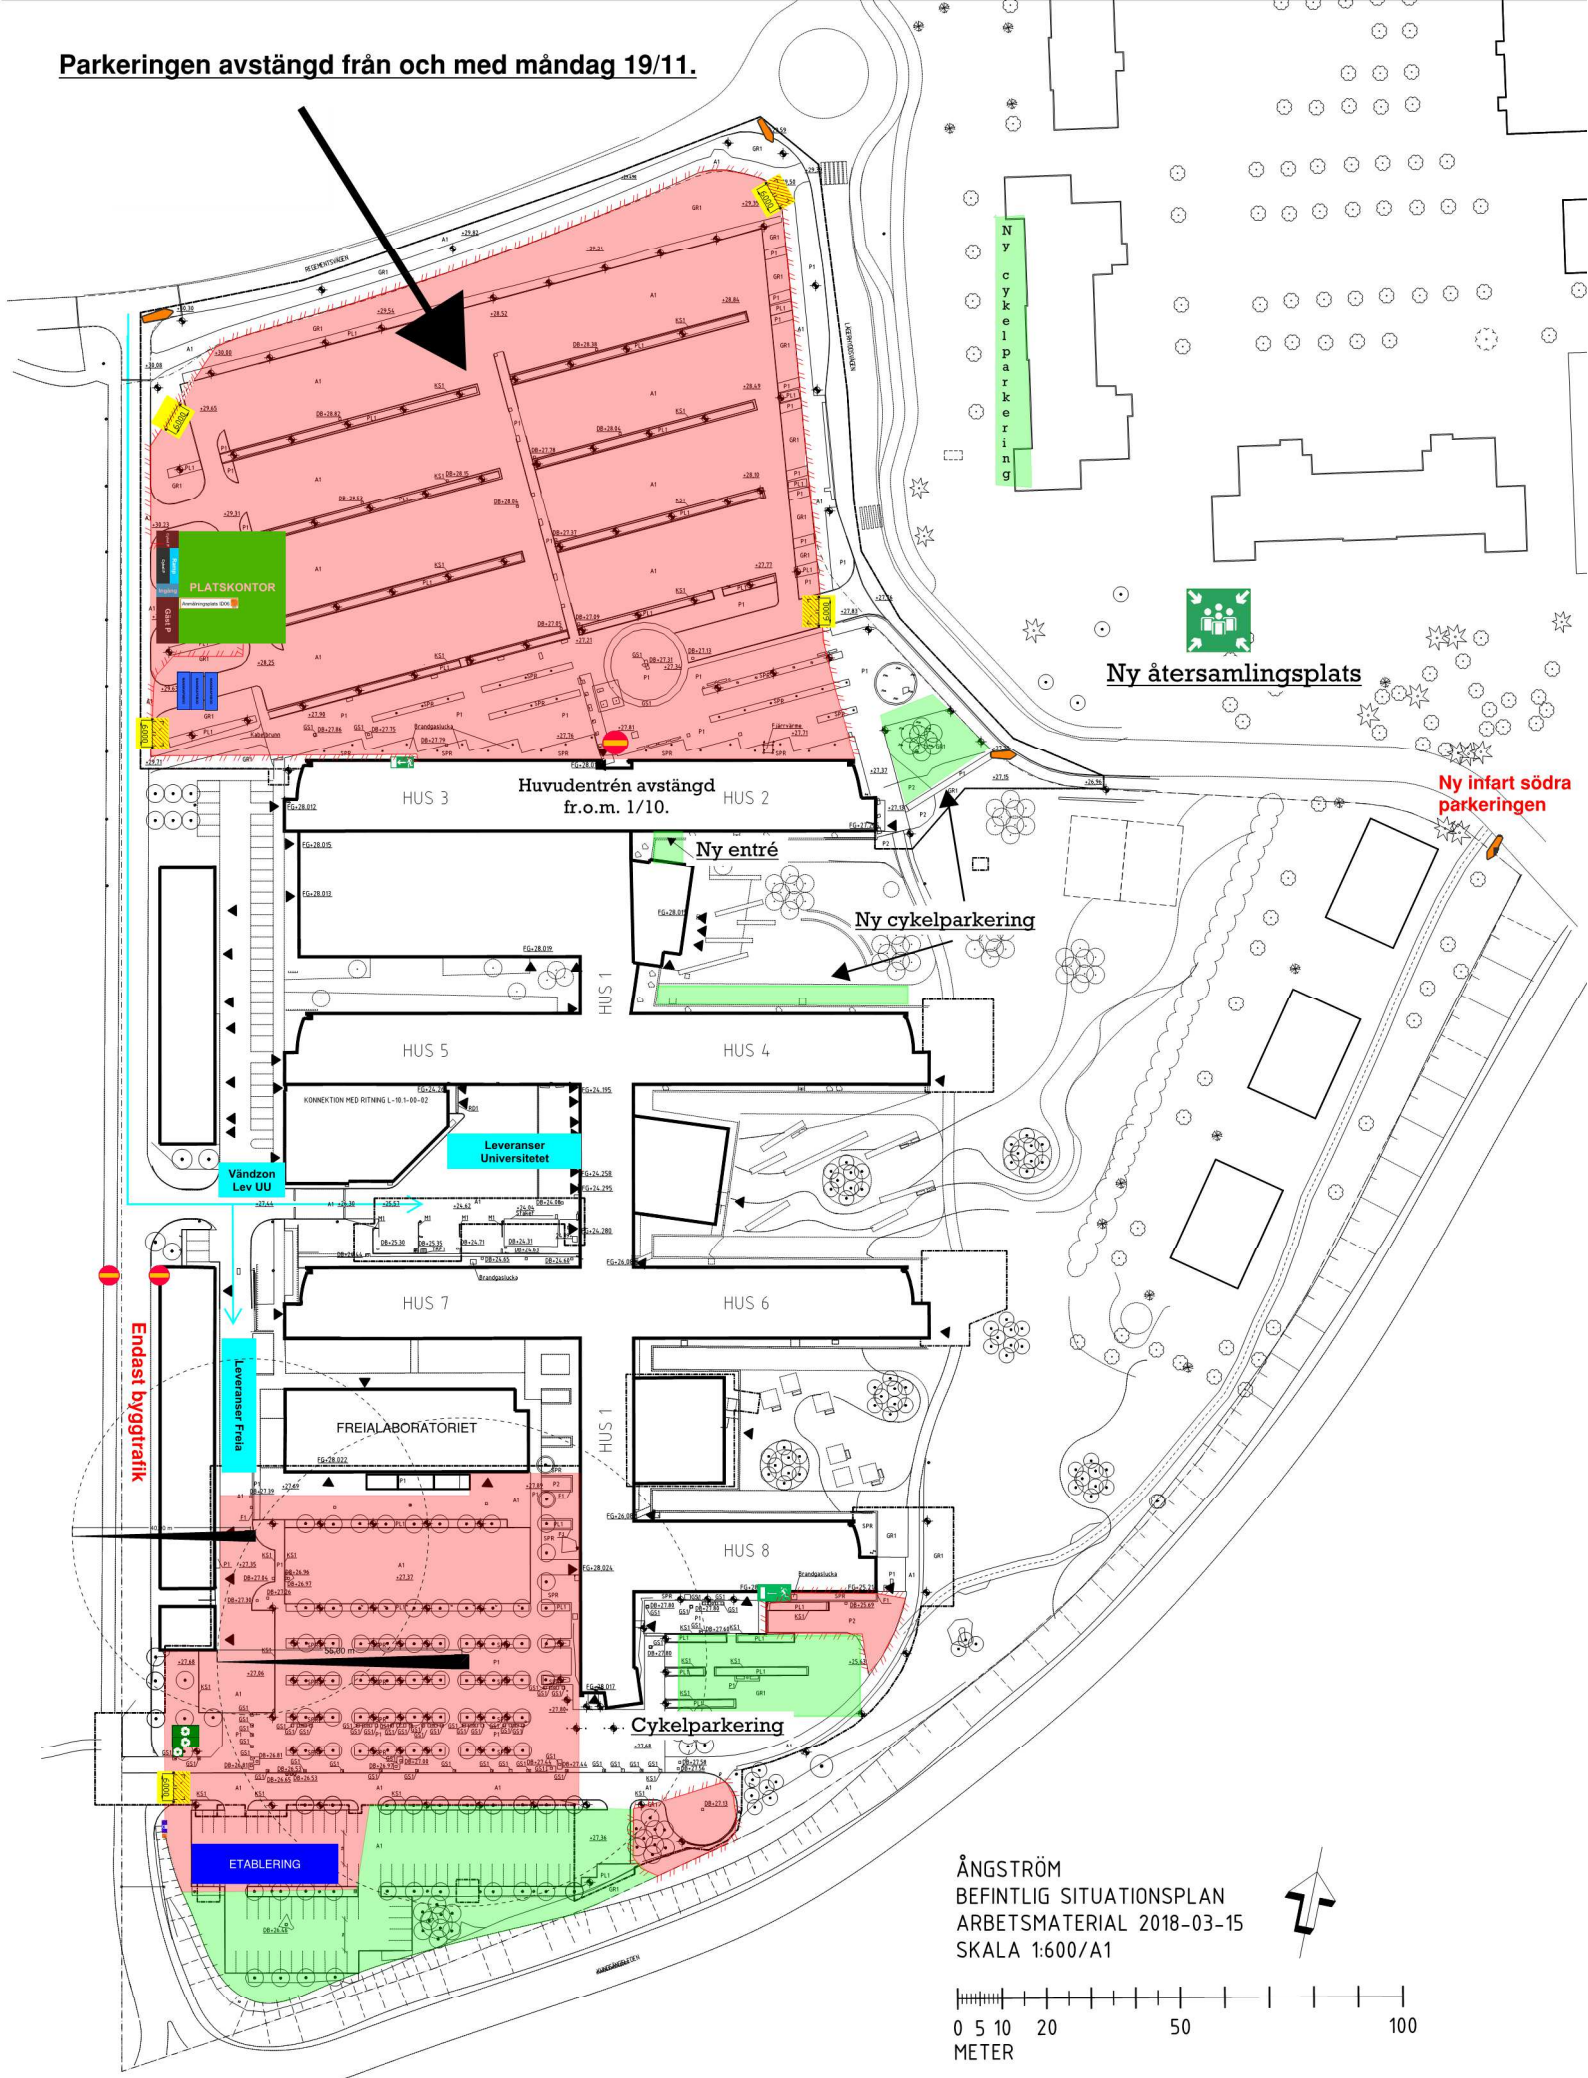

ÅNGSTRÖM
BEFINTLIG SITUATIONSPLAN
ARBETSMATERIAL 2018-03-15
SKALA 1:600/A1



APD-plan Å4
NCC
2018-12-19
