

## Weeks 26–33

### Work area Building 10

- Assembly of basement walls and framework.
- Refilling begins tentatively week 33
- Setting up of staff buildings.

### Work area Building 9

- Roof and facade work
- Interior, plastering and duct work.
- Installation of cables in ground

### Work area Building 8 and Southern Entrance

- Detail planning, foundation work.

### Work area Building 24

- Installation work.

### Work Area between Buildings 5 and 7 (Chemical Storage and Gas Line Installations)

- New gas line installation in consultation with affected organisations.
- Gas line installation in Building 1 between Buildings 5 and 7

### Work Area Building 1 (Existing Ångström)

#### Disturbances

- Heavy traffic.
- Large deliveries of framework for Building 10
- Interruption to gas deliveries during installation of new gas line. Impacted parties are kept informed in a special forum for new gas line installations.

#### Closures and Provisional Arrangements

- According to attached general plan.
- When the gas is turned on after the new line has been installed, areas around the goods reception will need to be closed. Parties particularly impacted will be informed of this separately. Begins earliest week 34.

#### Noticeable Upcoming Work (Preliminary Start Times)

- Connection of sprinklers Building 9, Autumn 2019.
- Cutting opening through concrete between Buildings 9 and 1, tentatively planned for summer 2019.
- Work with connecting Building 10 and Building 1, both installations and construction, late summer 2019.
- Removal of concrete foundation between Buildings 5 and 7. Earliest week 36.
- Construction of chemical storage between Buildings 5 and 7. Earliest week 36.

---

*Construction management for NCC and Akademiska Hus*



UPPSALA  
UNIVERSITET




AKADEMISKA HUS



Tornkran

Tornkran

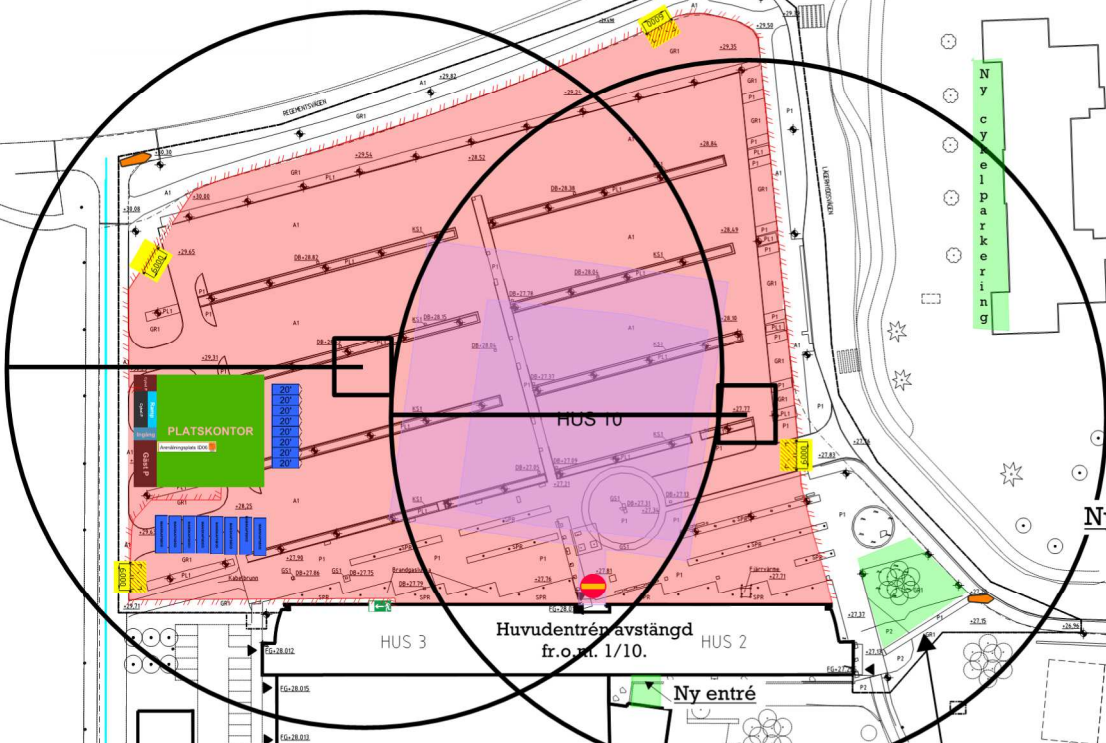

Ny cykelparkering



Ny återsamlingsplats

Ny infart södra parkeringen

Huvudentrén avstängd fr.o.m. 1/10.

Ny entré

Ny cykelparkering

HUS 5

HUS 4

HUS 7

HUS 6

FREILABORATORIET

HUS 9

HUS 8

ETABLERING

Cykelparkering

Endast byggetrafik

Vändzon Lev UU

Leveranser Universitetet

ÅNGSTRÖM  
 BEFINTLIG SITUATIONSPLAN  
 ARBETSMATERIAL 2018-03-15  
 SKALA 1:600/A1



APD-plan A4  
 NCC  
 2019-06-19

